


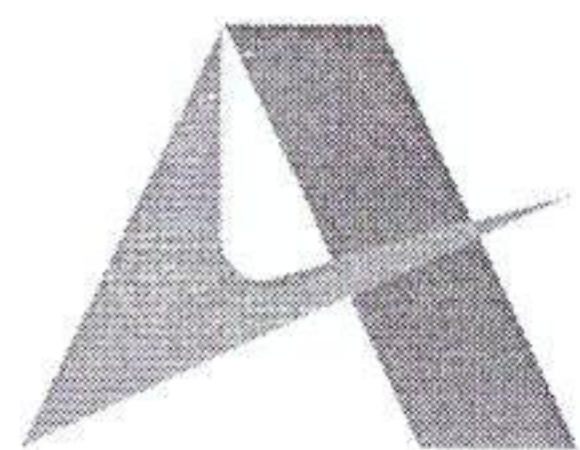

Contractor:
SHANDONG LUQIAO GROUP CO.LTD
OGRANAK BEOGRAD-Noví Beograd

MB: 29508739

PIB: 112302292

Address: TRG PRIJATELJSTVA SRBIJE I KINE 4

Bank Account: Bank of China Srbija A.D. Beograd
385-0202050005095-64



Subcontractor:

DOO PUT-INVEST NOVI SAD

MB: 08677212

PIB: 100398303

Address: Georgija Kneževića 3

Bank Account: Erste Bank a.d. Novi Sad
340-000000002110262

Civil and Track Construction (Lot NS-II) Project for Modernization and Reconstruction of Hungarian-Serbian Railway Connection in the Territory of the Republic of Serbia for Section Novi Sad-Subotica-Border (Kelebia)

Engineering Construction (Asphalt Work for Overpass Km152+282)

匈牙利-塞尔维亚铁路塞尔维亚境内诺维萨德-苏博蒂察-边境(克莱比奥)区段现代化与改造项目土建及轨道工程 (NS-II标段) (Km152+282桥梁沥青施工)

APPLICATION FOR FINAL PAYMENT CERTIFICATE

终期支付证书

NO. 2024-ERGS-XSTL-LW-024

202404

Value of works for this
measurement period (euro)

本期计量金额: 38,600.45

Cumulative value measured this
year (euro)

本年累计计量金额: 38,600.45

Value of approval for this
measurement period (euro)

本期批准金额: 38,600.45

Value of works up to the end of
this measurement period (euro)

截止本期累计计量金额: 38,600.45

Director of Contractor 承包商负责人: 

Seal of Contractor 承包商公章: 

Date of approval 批准日期: 19.04.2024.

Director of Subcontractor 分包商负责人: 

Seal of Subcontractor 分包商公章: 

Date of submission 提交日期: 19.04.2024.

Civil and Track Construction (Lot NS-II) Project for Modernization and Reconstruction of Hungarian-Serbian Railway Connection in the Territory of the Republic of Serbia for Section
Novi Sad-Subotica-Border (Kelebia) Engineering Construction (Asphalt Work for Overpass Km152+282)
匈牙利-塞尔维亚铁路塞尔维亚境内诺维萨德-苏博蒂察-边境(克莱比奥)区段现代化与改造项目土建及轨道工程（NS-II标段）(Km152+282桥梁沥青施工)

NO. 2024-ERGS-XSTL-LW-024

202404

No	Item	The amount according to the contract 合同金额(euro)	Value of works up to the end of the previous measurement period 截止上期计量金额(euro)	Value of works for this measurement period 本期计量金额 (euro)	Value of works up to the end of this measurement period 截止本期累计计量金额 (euro)
		a	b	c	d=b+c
I	Contract amount 合同金额	36,658.91		38,600.45	38,600.45
II	Total 总计	36,658.91		38,600.45	38,600.45
DOO PUT-INVEST NOVI SAD					
		Recorder编制:	Reviewer复核:	Director负责人:	
SHANDONG LUQIAO GROUP CO.LTD OGRANAK BEOGRAD-Novı Beograd					
		Contract Department: 合同部	Material Department: 机料科	Safety Department: 安全部	Engineering Department: 工程部
		Finance Department: 财务部	General Department: 综合办	Site Department: 施工处	Chief Engineer: 总工
		Director: 负责人	Leader in charge of Material Department: 机料科分管领导	Leader in charge of Site Department: 现场分管领导	

Asphalt Work for Overpass Km152+282

No.	Description	Unit	Contracted Works			Previously Completed Works		Work Completed of this Period		Cumulative Works of completions	
			Quantity	Unit price (euro)	Total Price (euro)	Quantity	Total Price (euro)	Quantity	Total Price (euro)	Quantity	Total Price (euro)
			a	b	c=b*a	d	e=b*d	f	g=b*f	h=d+f	i=b*h
1	ASPHALT CONCRETE WEARING COURSE- SMA 0/11 with PmB 45/80-65 4,0	m2	902.10	17.08	15,407.87			900.00	15,372.00	900.00	15,372.00
2	ASPHALT CONCRETE BINDER COURSE-AB11S with PmB 45/80-65 3,0 cm	m2	902.10	14.45	13,035.35			900.00	13,005.00	900.00	13,005.00
3	Prepare and close joints in concrete surface at the joints between asphalt and curb lines and at expansion joints with durably elastic mass.	m	341.40	5.50	1,877.70			312.00	1,716.00	312.00	1,716.00
4	Construction of leveling Layer with Concrete AB 11s (PmB 45/80-65)	t	23.00	192.67	4,431.41			34.26	6,600.87	34.26	6,600.87
5	Test for the completed works and submission the valid test	lump sum	1.00	1,906.58	1,906.58			1.00	1,906.58	1.00	1,906.58
TOTAL					36,658.91				38,600.45		38,600.45
DOO PUT-INVEST NOVI SAD			Recorder: 编制		Reviewer: 复核		Director: 负责人				
SHANDONG LUQIAO GROUP CO.LTD OGRANAK BEOGRAD-Novı Beograd			Contract Department: 合同部		Engineering Department: 工程部		Site Department: 施工处		Leader in charge of Site Department: 现场分管领导		
